


North Leg of Supreme  
Closed - Follow Detour

MATCH LINE STA 14+50  
SEE SHEET MOT-69

MOT LEGEND

- CONSTRUCTION WORK ZONE
- TEMPORARY PAVEMENT
- TYPE II BARRICADES OR DRUMS WITH STEADY BURNING LIGHT @ 50' CENTERS (25' CENTERS ALONG TAPERS)
- TYPE III BARRICADE WITH STEADY BURNING LIGHT
- TEMPORARY CONCRETE BARRIER (70400100)
- IMPACT ATTENUATORS, TEMPORARY (FULLY REDIRECTIVE, NARROW), TEST LEVEL 3 (70600260)
- CONSTRUCTION SIGN PER IDOT STANDARDS
- DIRECTION OF TRAFFIC
- TEMPORARY RAMP, SPECIAL (X4060995)
- VERTICAL PANEL WITH STEADY BURNING LIGHT 50 FT C-C
- EXISTING PAVEMENT MARKING
- PROPOSED PERMANENT PAVEMENT MARKING
- TEMPORARY PAVEMENT MARKING ALREADY IN PLACE

- ① PAVEMENT MARKING TAPE, TYPE III - LETTERS AND SYMBOLS (70300510)
- ② PAVEMENT MARKING TAPE, TYPE III - LINE 4" (SOLID, WHITE) (70300520)
- ③ PAVEMENT MARKING TAPE, TYPE III - LINE 4" (SOLID, YELLOW) (70300520)
- ④ PAVEMENT MARKING TAPE, TYPE III - LINE 4" (SOLID, DOUBLE YELLOW) (70300520)
- ⑤ PAVEMENT MARKING TAPE, TYPE III - LINE 4" (30' SKIP - 10' DASH, WHITE) (70300520)
- ⑥ PAVEMENT MARKING TAPE, TYPE III - LINE 6" (SOLID, WHITE) (70300540)
- ⑦ PAVEMENT MARKING TAPE, TYPE III - LINE 6" (6' SKIP - 2' DASH, WHITE) (70300540)
- ⑧ PAVEMENT MARKING TAPE, TYPE III - LINE 8" (SOLID, WHITE) (70300550)
- ⑨ PAVEMENT MARKING TAPE, TYPE III - LINE 12" (SOLID, YELLOW) (70300560)
- ⑩ PAVEMENT MARKING TAPE, TYPE III - LINE 12" (SOLID, WHITE) (70300560)
- ⑪ PAVEMENT MARKING TAPE, TYPE III - LINE 24" (STOP BAR, WHITE) (70300570)
- ⑫ THERMOPLASTIC PAVEMENT MARKING - LETTERS AND SYMBOLS (78000100)
- ⑬ THERMOPLASTIC PAVEMENT MARKING - LINE 4" (SOLID, WHITE) (78000200)
- ⑭ THERMOPLASTIC PAVEMENT MARKING - LINE 4" (SOLID, YELLOW) (78000200)
- ⑮ THERMOPLASTIC PAVEMENT MARKING - LINE 4" (SOLID, DOUBLE YELLOW) (78000200)
- ⑯ THERMOPLASTIC PAVEMENT MARKING - LINE 4" (30' SKIP - 10' DASH, WHITE) (78000200)
- ⑰ THERMOPLASTIC PAVEMENT MARKING - LINE 6" (SOLID, WHITE) (78000400)
- ⑱ THERMOPLASTIC PAVEMENT MARKING - LINE 6" (6' SKIP - 2' DASH, WHITE) (78000400)
- ⑲ THERMOPLASTIC PAVEMENT MARKING - LINE 8" (SOLID, WHITE) (78000500)
- ⑳ THERMOPLASTIC PAVEMENT MARKING - LINE 12" (SOLID, YELLOW) (78000600)
- ㉑ THERMOPLASTIC PAVEMENT MARKING - LINE 12" (SOLID, WHITE) (78000600)
- ㉒ THERMOPLASTIC PAVEMENT MARKING - LINE 24" SOLID WHITE (78000650)

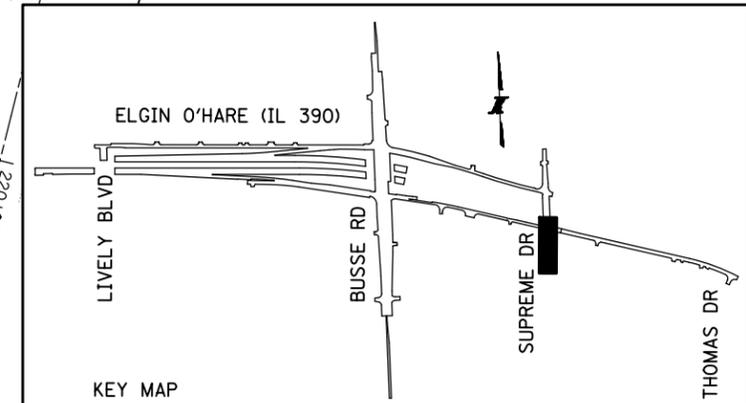

PEN TABLE = PEL.tbl  
 PLOT CFC = EDW.plt  
 USER NAME = kcooper@idm.com  
 PLOT DATE = 4/28/2015  
 FILE NAME = ...\\4041-2R\\1644.sht...MOT70-01.dgn  
 PLOT SCALE = 100.0000  
 PLOT DATE = 4/28/2015

DRAWN BY JAC DATE 04/22/15  
 CHECKED BY AAS DATE 04/28/15



THE ILLINOIS STATE TOLL HIGHWAY AUTHORITY  
 2700 OGDEN AVENUE  
 DOWNERS GROVE, ILLINOIS 60515

REVISIONS		
NO.	DATE	DESCRIPTION

CONTRACT NO. I-14-4644  
 MAINTENANCE OF TRAFFIC  
 MOT PLAN - STAGE 2A  
 SUPREME DRIVE

SHEET NO. MOT-70  
 DRAWING NO. 187 OF 1391

# 10 DAY ADVANCE LANE/SHOULDER CLOSURE REQUEST

**DAY:** Permanent

*Sun, Mon, Tues, Wed, etc.*

**NIGHT:** Permanent

*Sun, Mon, Tues, Wed, etc.*

**DATE:** 4/19/16-8/15/16

*Date of Closure(s)*

Tollw'y #	Contract # or Maint. bldg.	CLOSURE from M.P. to M.P.	DIR.	Nearest underpass/overpass X-RD to X-RD	TYPE OF WORK	LANE(S) or SHLD CLOSED	LANE(S) OPEN	TIMES of CLOSURE
OFF Supreme Dr.	I-14-4644	South of Thorndale	NB/SB	Thorndale/Supreme	Staged Reconstruction – Reduced lane widths	None – Traffic shifted east	1 Lane in each direction	4/19/16 7:00 AM to 8/15/16 7:00 AM
I-								
I-								
I-								
I-								
<b>Cancellation notices must be received ASAP with copies also sent to the Traffic Center Staff at <a href="mailto:TIMSTOC@getipass.com">TIMSTOC@getipass.com</a>.</b>								
<b>Why Necessary?</b>	<i>Begin reconstruction of south leg of Supreme Dr. Lane widths will be reduced to 11'. The north leg of Supreme will be closed and a detour route posted.</i>							
<b>How Reducing Impact?</b>	<i>Traffic signals will be maintained at Supreme/Thorndale to facilitate turn movements.</i>							

All closure requests must be submitted to Lane Closures by e-mail, **no later than 9am 10 days in advance** of the start of new construction or any major change in traffic. **Designate a read and/or delivery receipt within the e-mail to assure delivery.** *Follow up with a phone call **ONLY** if the e-mail read/delivery receipt is not verified.* A copy of this request should also go to Jan Kemp and Maria Burnham in Communications as well as Elyse Morgan in the Traffic Center and to the Traffic Center Staff.

**e-mail:** [laneclosures@getipass.com](mailto:laneclosures@getipass.com)  
[jkemp@getipass.com](mailto:jkemp@getipass.com)  
[mburnham@getipass.com](mailto:mburnham@getipass.com)  
[emorgan@getipass.com](mailto:emorgan@getipass.com)  
[timstoc@getipass.com](mailto:timstoc@getipass.com)

**Phone#:** (630)241-6800 ext. 3822  
 (630)241-6800 ext. 2381  
 (630)241-6800 ext. 2389  
 (630)241-6800 ext. 3703  
 (630)241-6800 ext. 3703

**Cell#:**  
 (630)364-9751

Date submitted to Tollway: 4/8/16 Time submitted to Tollway: 5:00 PM Project # I-14-4642

Name: Cheryl Ludwig Co: V3 Companies Title: CCM Phone#: 630.303.8164
